




Monthly Progress Report

March 2025

Cutchogue Fire Department

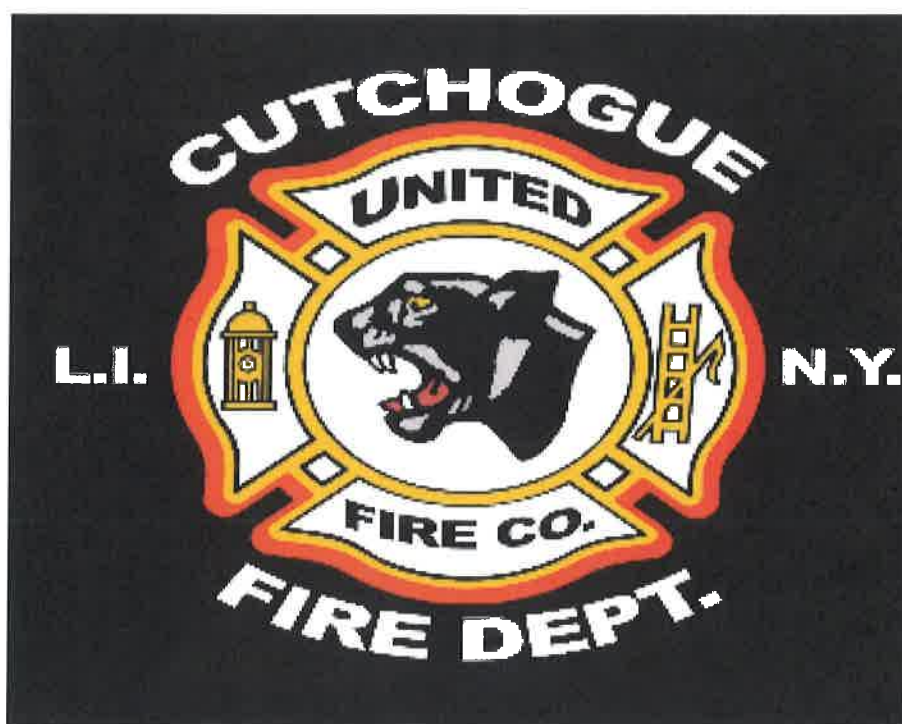

Report prepared by Clinton Mellas





Table of Contents

Section I – Project Summary

Section II – Work Progress for March 2025

Section III – Work Projected for April 2025

Section IV – Progress Photo

Section V – Monthly Workforce Summary

*Providing Leadership,
Integrity, and Building
Excellence since 1989*



Section I – Program Summary

March 2025

- Cutchogue Fire Department- New Building



Section II - Work Progress

March 2025

- MEP roughing in 1st and 2nd floors, Ductwork, Copper piping, Electrical conduits.
- Installation complete of interior CMU block walls.
- Additional layer of roof sheathing complete.
- Fascia boards completed on SIP panels.
- Installation of exterior waterproofing, insulation, and stone has begun on the North, South and West side of building.
- Electrical Transformer set on vault on southwest corner of property.



Section III – Work Planned April 2025

- Continuing installation of CMU for South Elevator shaft.
- Electricians pull wires, rough for lighting fixtures, outlets, etc.
- Plumber Installing Roof drains and roughing for 2nd Floor bathrooms.
- Mechanical (HVAC) installing gas piping to RTU's and refrigerate lines to split systems.
- Continue to Install exterior insulation, waterproofing, and Stone.
- Installation of flat roof.
- Continue installation of Stone and brick on All elevations.



Section IV – Progress Photos



Waterproofing sealant, and flashing.



Section IV – Progress Photos



Exterior brick on NW side of building



Section IV – Progress Photos



South Elevator Shaft



Section IV – Progress Photos



Flat roof insulation



Section IV – Progress Photos



Brick and Stone on SW side of building

Section IV – Progress Photos



Electrical transformer



Section IV – Progress Photos



RTU 1




Section V – Workforce Summary – Company/Hours

March 2025

Manpower Graph

82 Contracting Inc. Commander Electric, Inc. Park East Construction Corp. Stalco Construction Ultimate Power Inc. Enviroscience
DKM Steel Construction Corp. Maccarone Plumbing Inc.

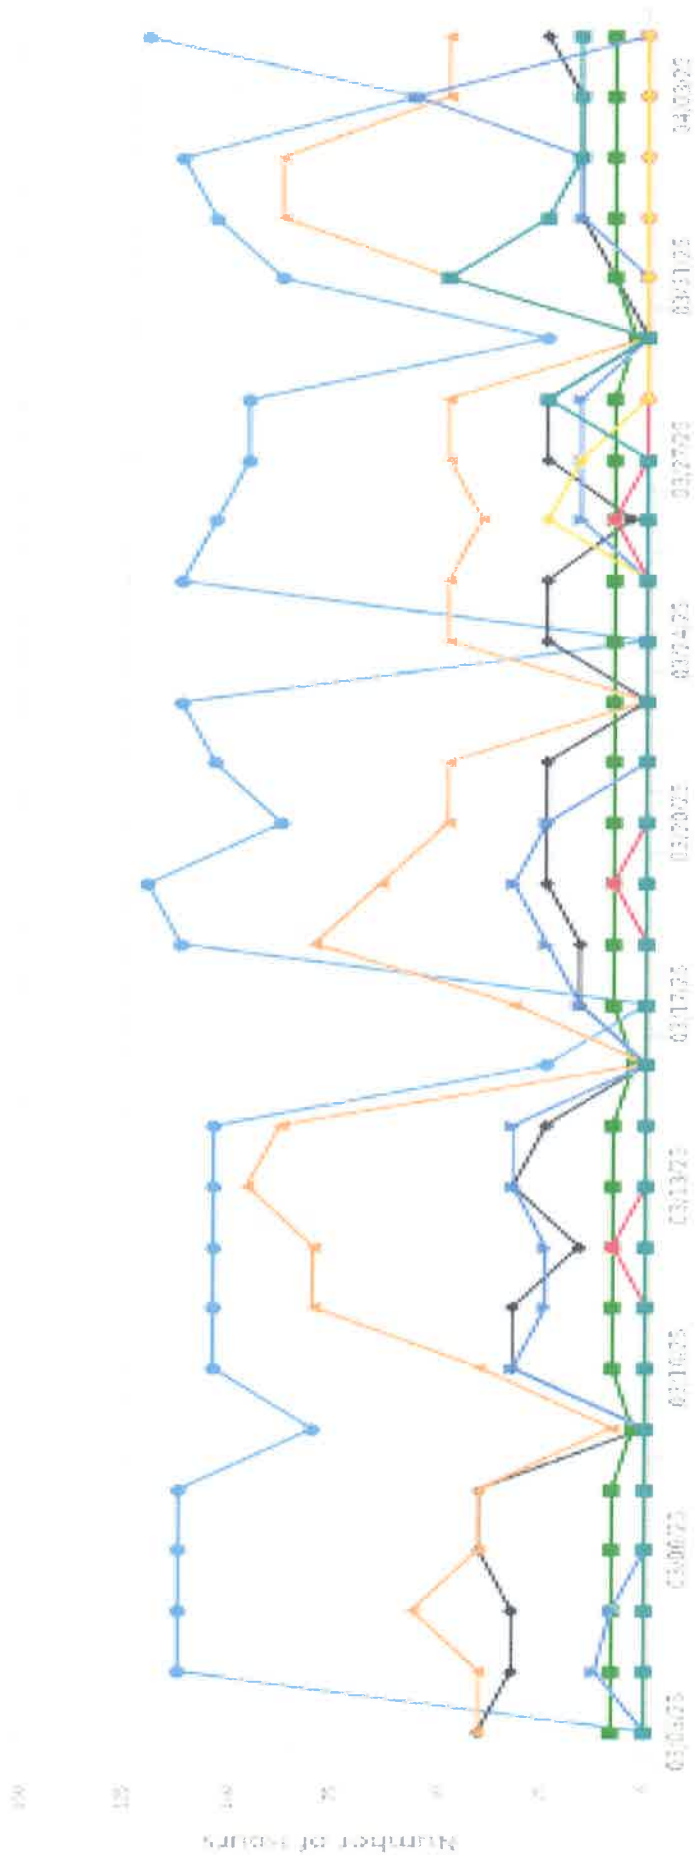



Cutchogue Fire Department
March 2025

End of Progress Report
