




# Monthly Progress Report

April 2025

Cutchogue Fire Department

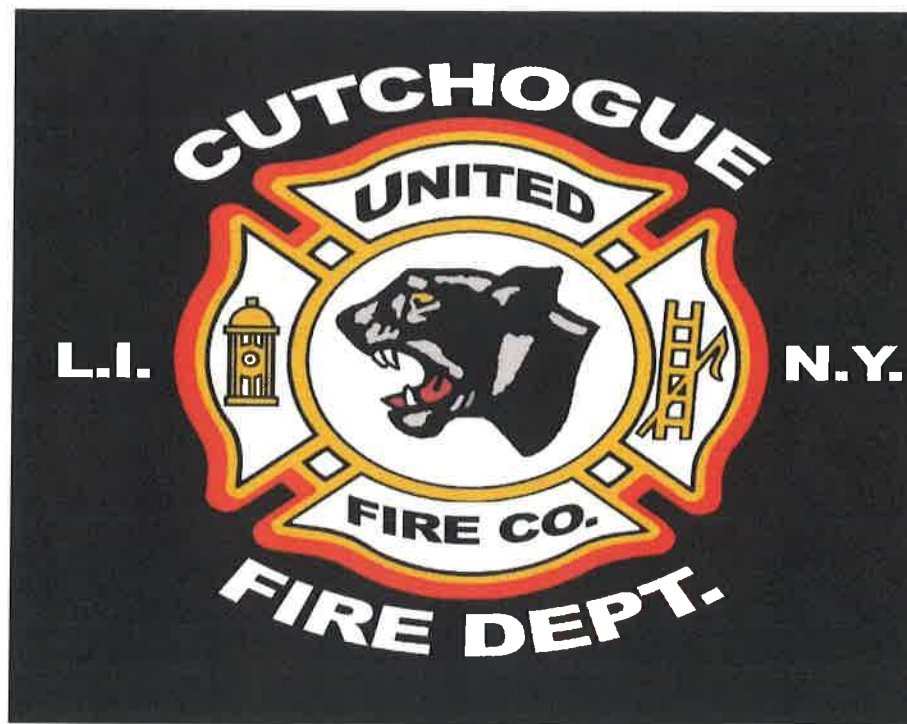

Report prepared by Joseph Adragna





## Table of Contents

**Section I – Project Summary**

**Section II – Work Progress for April 2025**

**Section III – Work Projected for May 2025**

**Section IV – Progress Photo**

**Section V – Monthly Workforce Summary**

*Providing Leadership,  
Integrity, and Building  
Excellence since 1989*



## Section I – Program Summary

### April 2025

- Cutchogue Fire Department- New Building



## Section II - Work Progress

### April 2025

- Finished installation of CMU for South Elevator shaft and brick for North curtain wall.
- Heat piping and ductwork insulation began throughout the building.
- Generator Steel Dunnage was installed
- Electricians pulled wires, roughed for lighting fixtures, outlets, on 2<sup>nd</sup> floor.
- Plumber Installed Roof drains and began rough-in of 2<sup>nd</sup> Floor bathrooms.
- Mechanical (HVAC) installed gas piping to RTU's and refrigeration lines to split systems.
- Installed exterior insulation, waterproofing, and Stone.
- Installed the flat roof.
- Continue installation of Stone and brick on All elevations.



## Section III – Work Planned May 2025

- Complete installation of Stairwell B bulkhead.
- Finish roofing on the south side of building and complete ridge vents.
- Electricians lay out lighting on the 1st floor and complete the 2nd floor rough-in.
- Electrical panels are to be installed in the 2nd floor electrical closet.
- Plumber to complete rough-in of 2<sup>nd</sup> Floor bathrooms and kitchen/bar areas.
- Sprinkler piping begins on the second floor.
- Mechanical (HVAC) to install VAVs and cabinet heaters on the 2<sup>nd</sup> floor.
- Continue to Install exterior insulation, waterproofing, and Stone.
- Complete brick and stone on the south and west sides of the building.
- Continue brick and stone of the north and east sides of the building.
- Installation of the north curtain wall.
- Installation of the elevators scheduled to begin.



## Section IV – Progress Photos



South Elevation and Stairwell B





## Section IV – Progress Photos



North Curtain Wall



## Section IV – Progress Photos







## Section IV – Progress Photos



Generator Steel Dunnage




## Section IV – Progress Photos



Electrical Grounding Bridge



## Section IV – Progress Photos

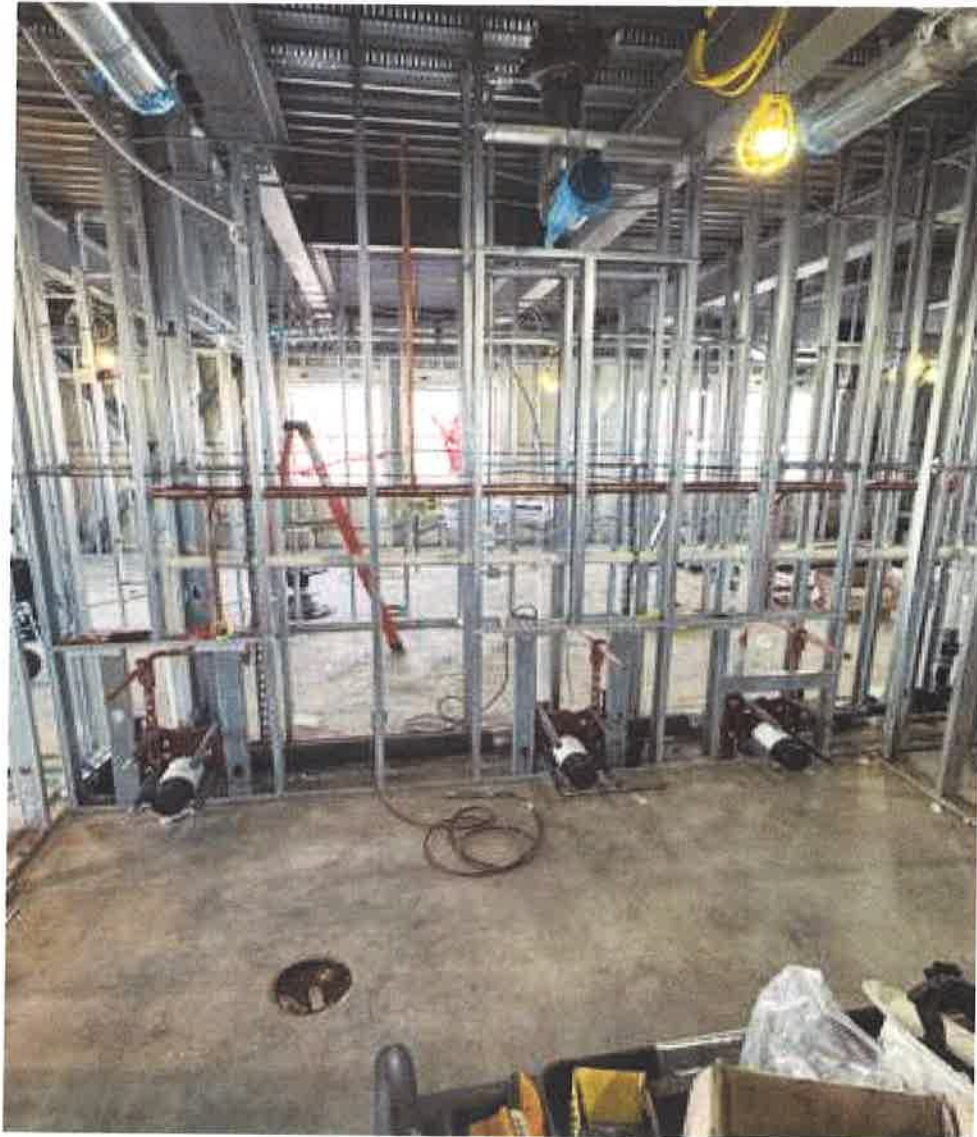

2<sup>nd</sup> Floor Woman's Bathroom





## Section IV – Progress Photos



Southwest Corner of the Firehouse




## Section V – Workforce Summary – Company/Hours

April 2025

### Manpower Graph

82 Contracting Inc. • Park East Construction Corp. • Commander Electric, Inc. • MacCarone Plumbing Inc. • Stalco Construction • DKM Steel Construction Corp  
Ultimate Power Inc.

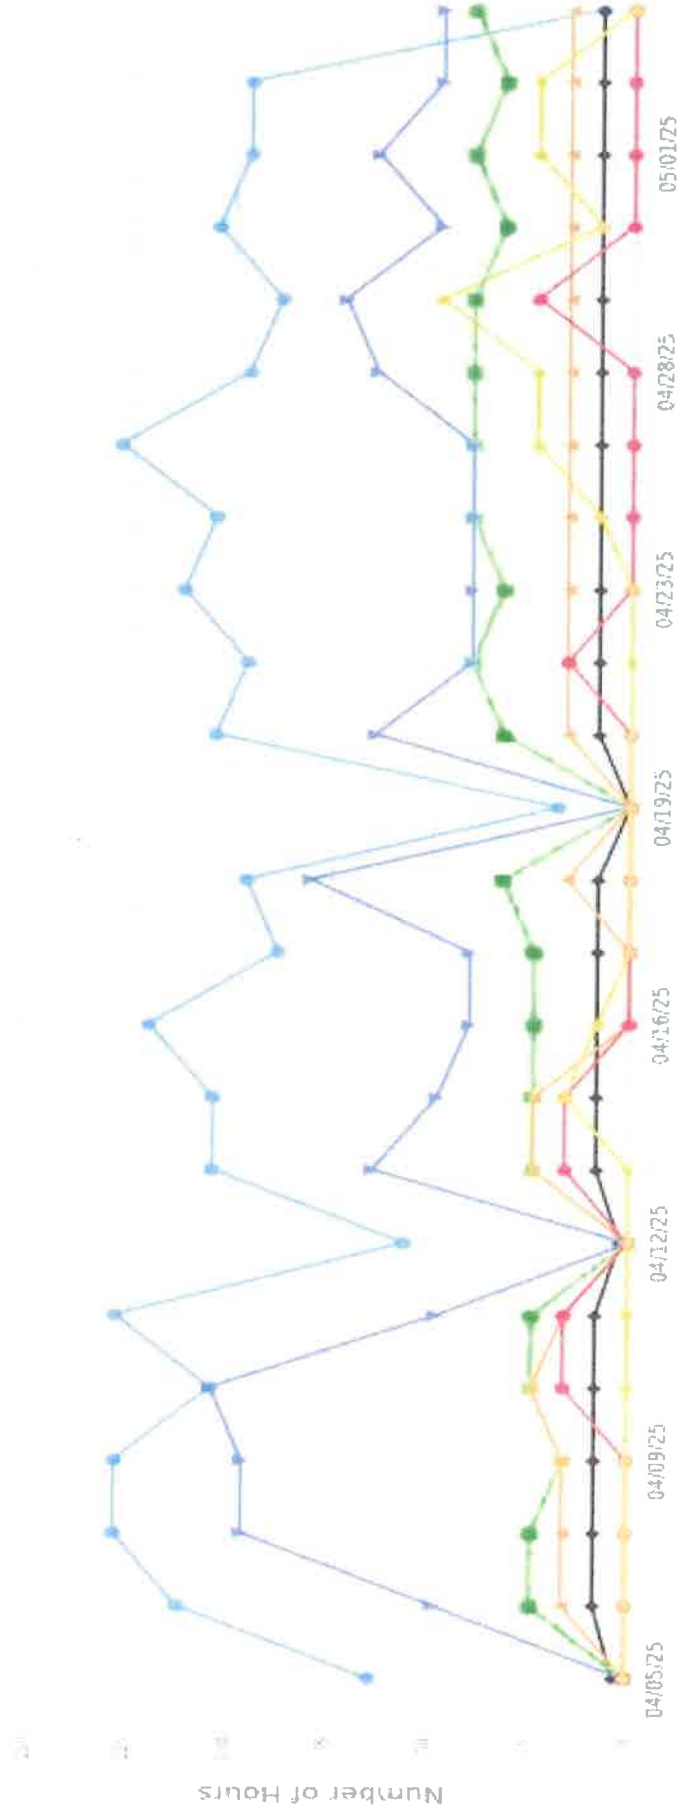





Cutchogue Fire Department  
April 2025

End of Progress Report
