



# Monthly Progress Report


RECEIVED

February 2025

MAR 14 2025

CUTCHOGUE  
Fire District

## Cutchogue Fire Department

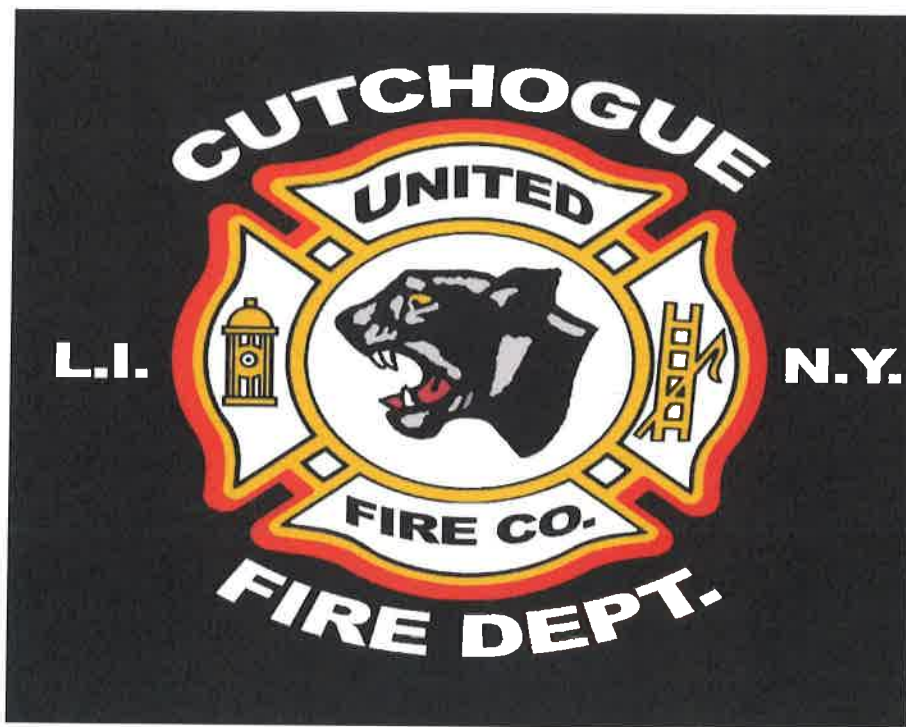

Report prepared by Clinton Mellas





## Table of Contents

**Section I – Project Summary**

**Section II – Work Progress for February 2025**

**Section III – Work Projected for March 2025**

**Section IV – Progress Photo**

**Section V – Monthly Workforce Summary**

*Providing Leadership,  
Integrity, and Building  
Excellence since 1989*



## Section I – Program Summary February 2025

- Cutchogue Fire Department- New Building



## Section II - Work Progress

### February 2025

- MEP roughing in 1<sup>st</sup> and 2<sup>nd</sup> floors, Ductwork, Copper piping, Electrical conduits.
- Installation of interior CMU block walls and South elevator shaft.
- Installation of Roof SIP panels complete.
- Additional layer of roof sheathing complete.
- Fascia boards completed on SIP panels.
- Installation of exterior waterproofing, insulation, and stone has begun on the North side of building.
- Electrical Vault is set in southwest corner of property.



## Section III – Work Planned March 2025

- Continuing installation of interior CMU block wall and South Elevator shaft.
- MEP's continuing to install electrical panels, electrical feeders, copper piping.
- Continue to Install exterior insulation, waterproofing, and Stone.
- Install roof shingles on SIP Panels.



## Section IV – Progress Photos



Waterproofing sealant, and flashing.



## Section IV – Progress Photos



SIPs Panels & fascia complete, ice & water shield and tar paper on roof.



## Section IV – Progress Photos



Arriscraft exterior base stone on North side of building.





Roof framing on top of SIP panels



Community Gathering Room



Commissioner's Office
