




Monthly Progress Report

May 2025

Cutchogue Fire Department

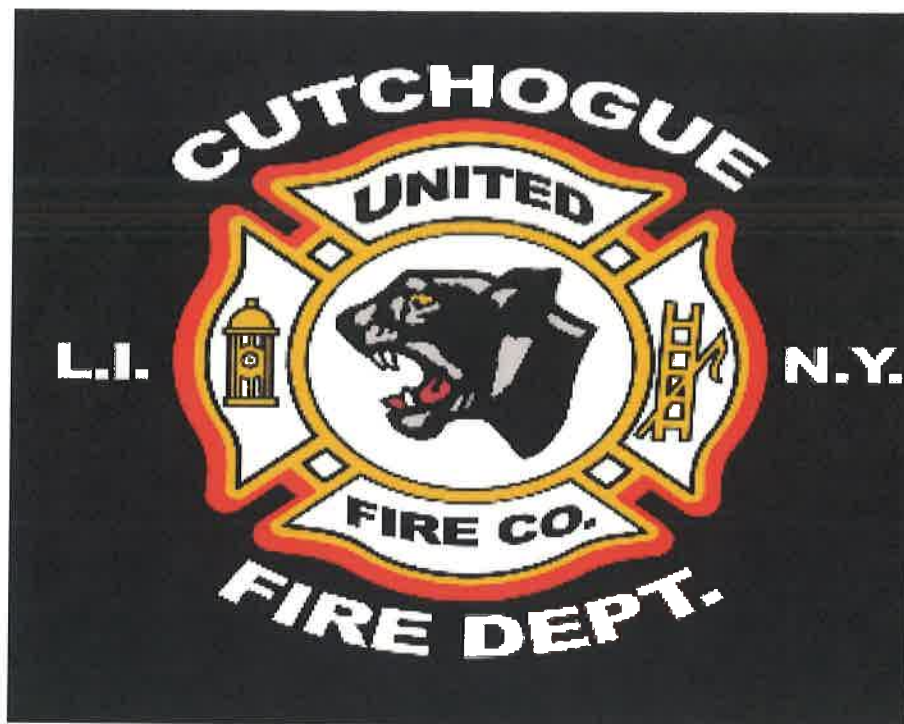

Report prepared by Joseph Adragna





Table of Contents

Section I – Project Summary

Section II – Work Progress for May 2025

Section III – Work Projected for June 2025

Section IV – Progress Photo

Section V – Monthly Workforce Summary

*Providing Leadership,
Integrity, and Building
Excellence since 1989*



Section I – Program Summary May 2025

- Cutchogue Fire Department- New Building



Section II - Work Progress

May 2025

- Brick and stone on the south and west sides of the building was completed.
- The north curtain wall was installed.
- The installation of Stair B began.
- The installation of stairwell B bulkhead was completed.
- Brick and stone continued to be laid on the north and east sides of the building.
- Sheetrock began being installed on the 2nd floor.
- The rooftop generator was installed
- Electricians installed lighting on the 1st floor and continued the 2nd floor rough-in.
- Electrical sub-panels were installed in the 2nd floor electrical closet.
- The electrical service was completed with permanent power.
- Plumbers continued to rough-in the 1st and 2nd floors.
- Sprinkler piping began on the second floor.
- VAVs and exposed oval ductwork installation on the 1st and 2nd floors began.



Section III – Work Planned

June 2025

- Brick and stone will continue along the east and north sides of the building.
- Installation of the east facing 2nd floor windows.
- The PVC fascia will continue along the building's soffit.
- Staircases A and B will be installed.
- Sheetrock and spackling will continue throughout the building.
- The 2nd floor ceilings will begin being painted.
- The 2nd floor interior doors will start to be installed.
- The installation of elevators A and B will start.
- The conduits for lighting, power, fire alarm and HVAC will be completed.
- Ongoing fire suppression system installed throughout the building.
- The Fuji septic system will be installed.



Section IV – Progress Photos



South Elevation




Section IV – Progress Photos



North Curtain Wall



Section IV – Progress Photos

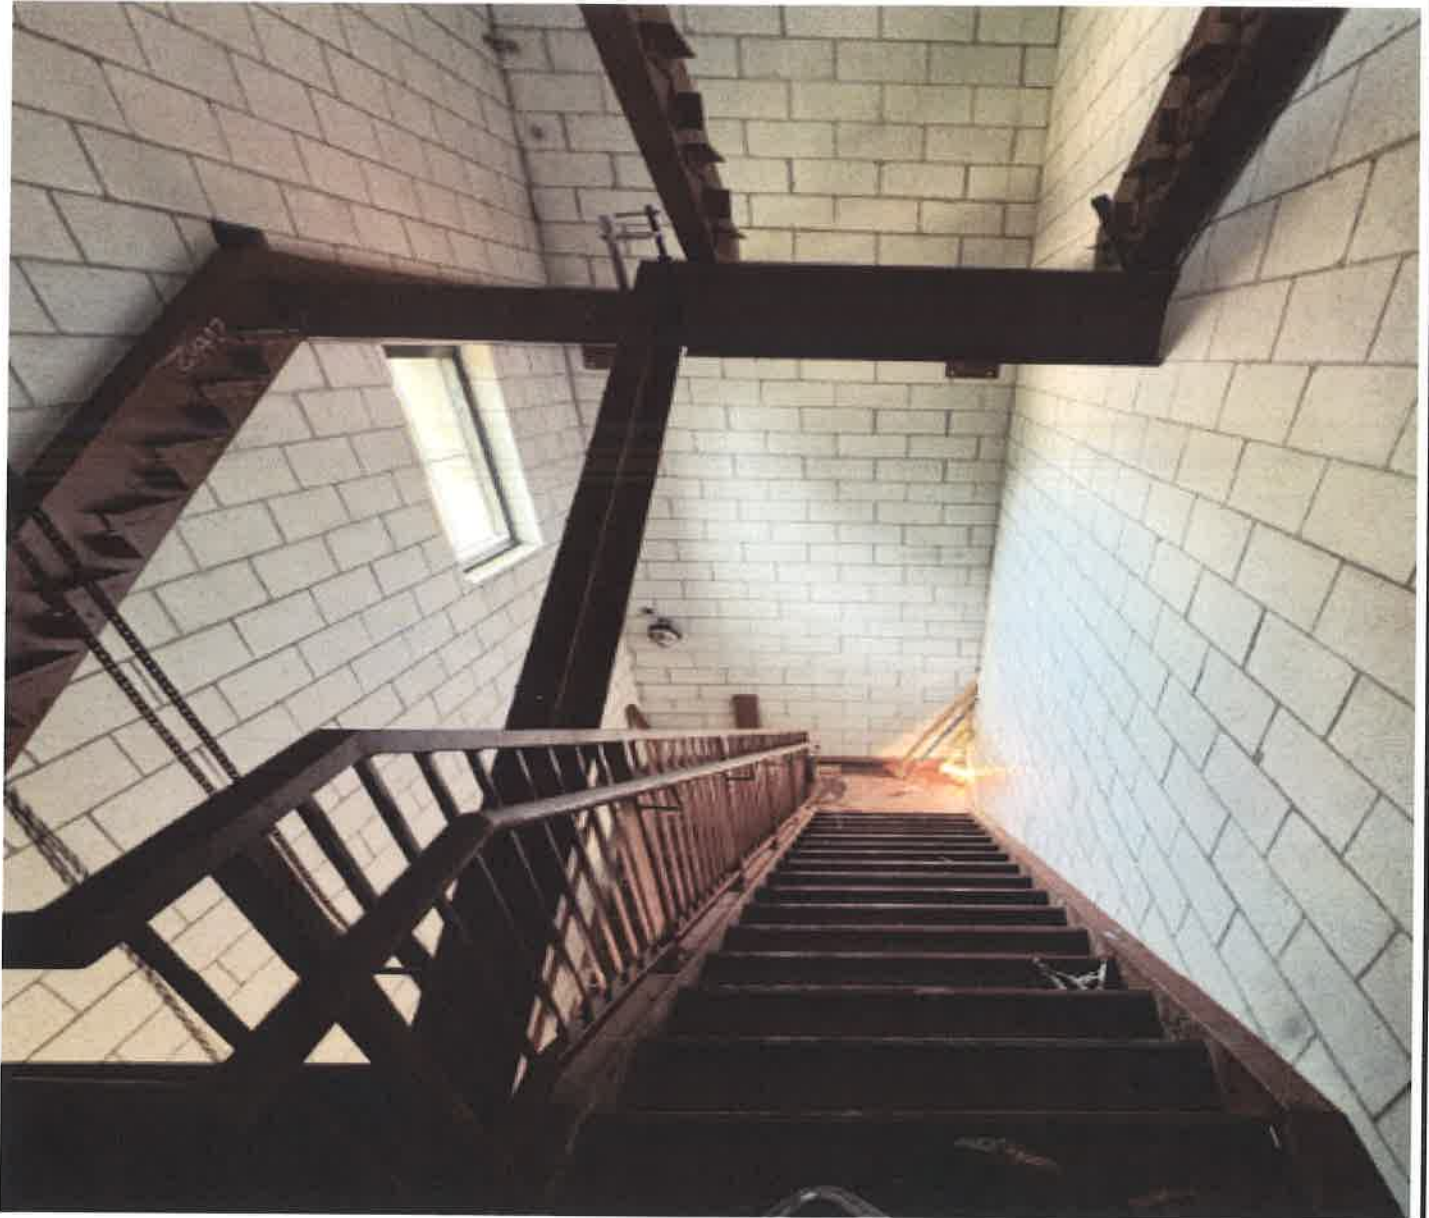

Stairwell B



Section IV – Progress Photos



Rooftop Generator



Section IV – Progress Photos



1st Floor Radio Room Bathroom



Section IV – Progress Photos



Oval Ductwork and Fire Suppression in the Gathering Hall



Section IV – Progress Photos




Exposed Oval Ductwork in the Lobby/Lounge



Section V – Workforce Summary – Company/Hours

May 2025

MANPOWER GRAPH

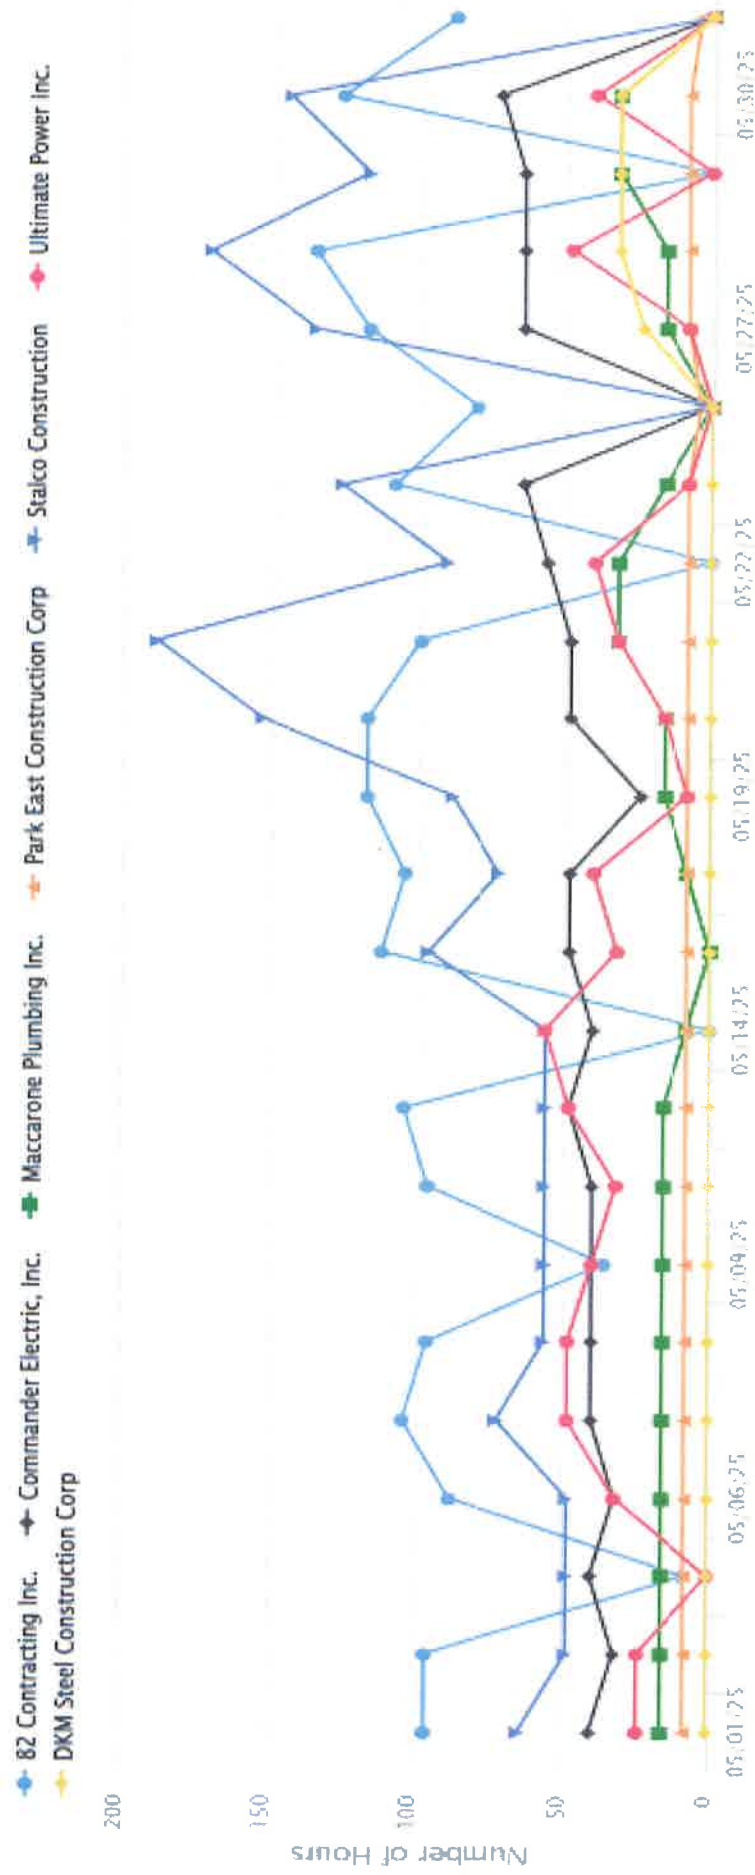



Cutchogue Fire Department

May 2025

End of Progress Report
